Public Facilities Update




Agenda

- Construction Manager at Risk Process
- Budget Update
- Cost Reductions
- Add Alternates
- Next Steps



Construction Manager at Risk Process

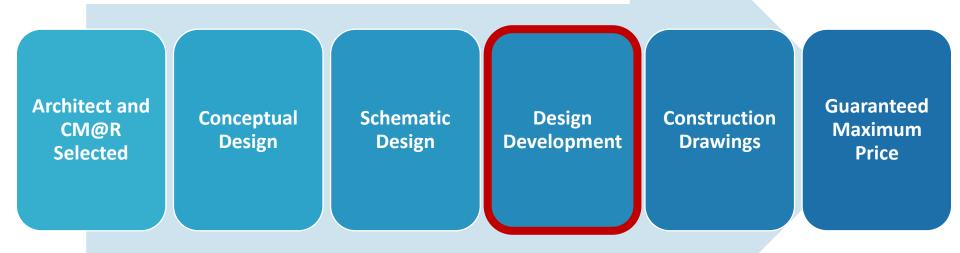



June 11, 2019 Budget Discussion

	Option A	Option B	Option C
PD and FD	2,460,000	2,460,000	2,460,000
AV, Security	400,000	400,000	400,000
251 Base price	7,770,088	7,770,088	7,770,088
Asbestos removal	60,000	60,000	60,000
2-story lobby		750,000	620,000
Operable partitions (4)	160,000	160,000	160,000
Sub-total construction	10,850,088	11,600,088	11,470,088
Soft Costs (30%)	3,255,026	3,480,026	3,441,026
Total	14,105,114	15,080,114	14,911,114
Issuance Cost	300,000	300,000	300,000
Grand Total	14,405,114	15,380,114	15,211,114



Current Budget Estimate

Option A Total Budget: Construction + Soft Costs	14,105,114
Current Construction Cost Estimate	11,782,000
Design + Preconstruction Fees	1,115,248
Total	12,897,348
Remaining Soft Costs/Contingency/FFE	1,207,766




- Site plan modifications
- Exterior and interior material modifications
 - Reduce tile in restrooms, type of carpet
 - Addition connector changed to painted fiber cement board versus pre-cast concrete
 - Use acoustical ceiling tiles in office areas and community rooms
 - Reduce exterior signage
 - Clean terrazzo floors but not refinish
- Mechanical system modifications
- Reduction in sally port size






Addition connector changed to painted fiber cement board versus pre-cast concrete



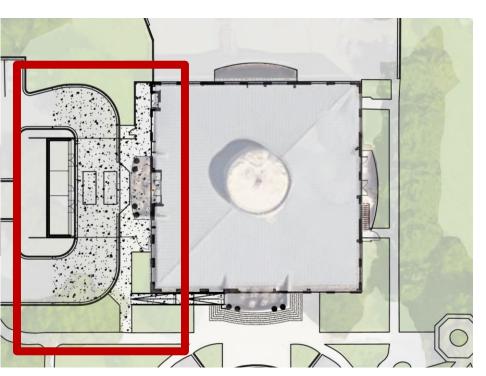

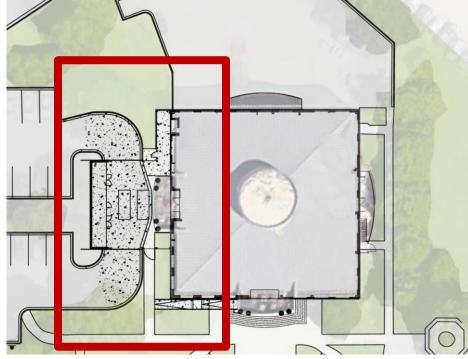

Width of sally port reduced, width of storage closets reduced, material changes from concrete to asphalt, keep current sidewalk on side of building instead of demolition and rebuild





Parking spaces reduced, concrete walls removed, some stormwater modifications. Additional reductions possible.



Add Alternate Options

- Stormwater
 - Above ground versus underground retention
 - Above ground cost is \$150,000
 - Underground is \$250,000
- Auditorium Lobby
 - Open up ceiling and staircase or leave as is
 - Cost to open and remove staircase is \$300,000



Add Alternate Options





Above ground retention show on left, below ground on right



Potential Budget Changes

Option A Total Budget: Construction + Soft	
Costs	14,105,114
Current Construction Cost Estimate	11,782,000
Add Alternate Option Stormwater	
Above Ground	-100,000
Add Alternate Option Auditorium	
Lobby Stays as is	-300,000
Design + Preconstruction Fees	1,115,248
Total Range	12,897,348 to 12,497,348
Remaining Soft Costs/FFE/Contingency	
Range	1,207,766 to 1,607,766



Next Steps

- Proceed to construction design phase
- October 2020 April 2021:
 - Permitting
 - Bidding
 - Guaranteed Maximum Price
- GO Bond Issuance May

